


PLAN AND PROFILE
OF THE
RELIEF DRAIN FROM SOUTH TALBOT ROAD TO 7
TOWNSHIP OF SANDWICH SOUTH
COUNTY OF ESSEX, ONTARIO

Plan Scale - 20 ch. to 1 in.
Profile Scale - Hor. 6 ch. to 1 in.
Ver. 6 ft. to 1 in.

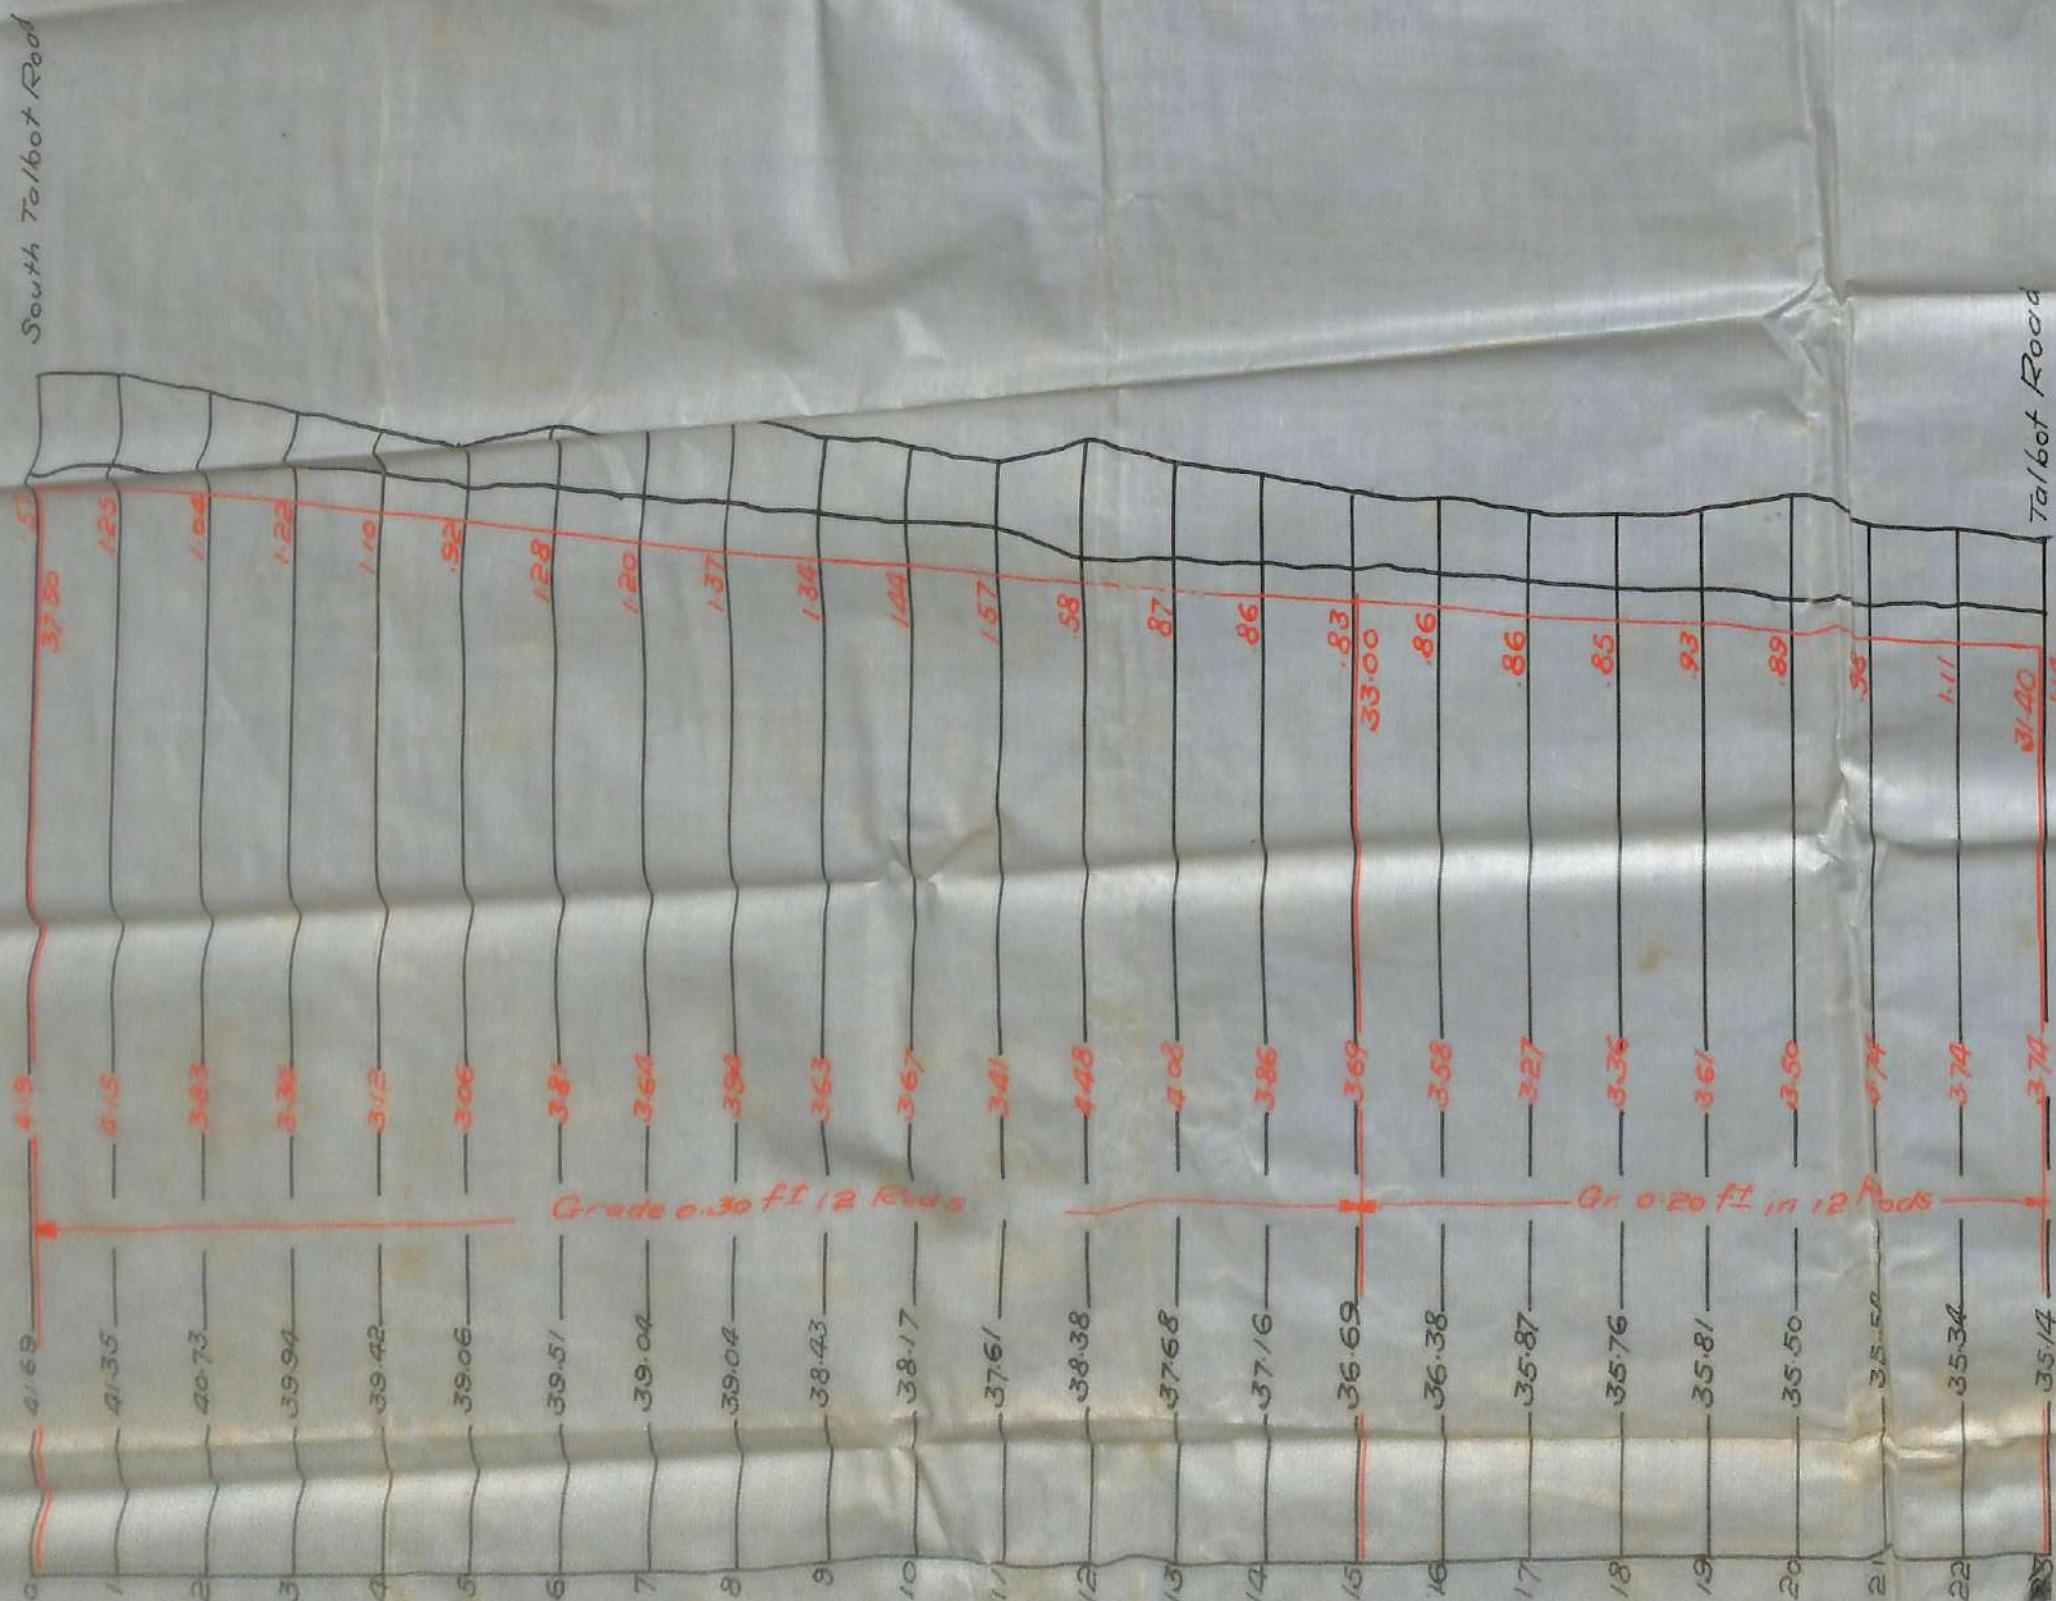

PLAN

OF THE


RELIEF DRAIN FROM SOUTH TALBOT ROAD TO TALBOT
TOWNSHIP OF SANDWICH SOUTH
COUNTY OF ESSEX, ONTARIO

Plan Scale - 20 ch. to 1 in.
Profile Scale - Hor. 6 ch. to 1 in.
Ver. 6 ft. to 1 in.

C. W. McKay.

Civil Engineer

Walkerville July 15th 1913.

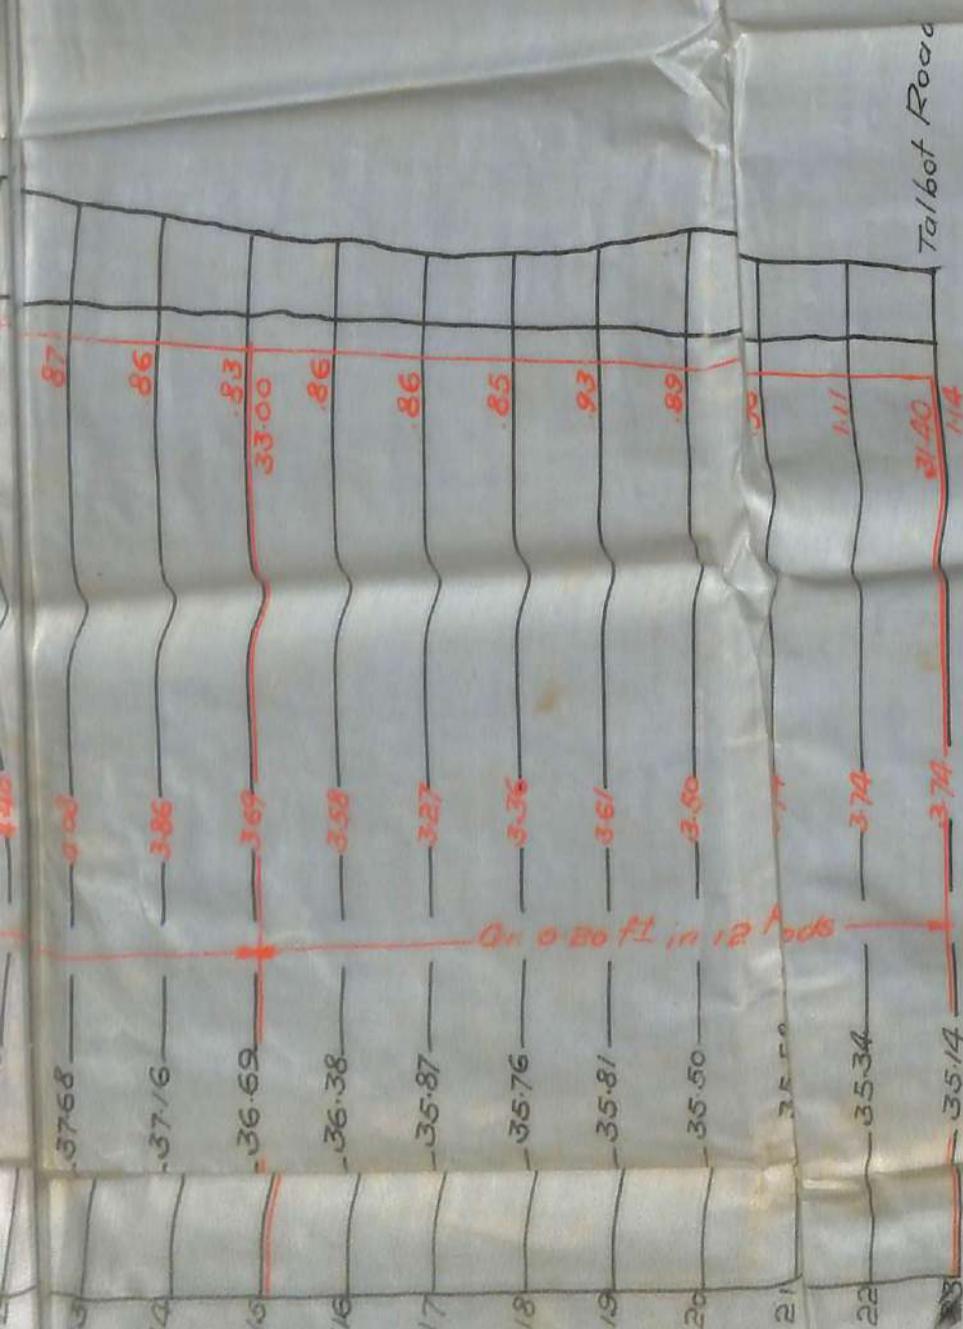

TO TALBOT
SOUTH
ARIO

Cwm McKay.
Civil Engineer
Walkerville July 15th 1913.



(2)

Continued from page I

Malden Road Relief Branch.

South Talbot Road to Blind Line	
I38 rods of Ditching @ 87¢ per rod	114.84
Blind Line to Delisle Drain	
I42.1/2 rods of ditching @ 96¢ per rod	136.80
Cost of excavation.	251.64

Removing Brush, small trees &c

30.00

Allowances to owners for earth spread on land

33.00

Cutting and replacing line fence to allow teams
to pass through

4.00

Damages to meadows and crops if any,

15.00

Amount of Extravagancies

71.00

Cost of Construction

322.64

Summary of estimated cost of the Delisle Drain
System as follows

East branch including 84 rods on Talbot Road 819.06

West Branch

654.79

Malden Road Relief Branch

322.64 1796.49

Incidental charges.

Court of Revision 18.00

Printing and Distributing By-Law 20'00

Clerks Fees 30.00

Surveys, Plans and Estimates 75.00

Assistants on Survey 24.00

Selling and Superintending work 75.00

Total Incidentals 843.00

2051.09

Omer M. Key

N.B. The Delisle Drain East and West
Branches and Relief drain were included
in one By Law

Omer M. Key

Money Paid Contractor on Rely drain to date
The Township of Sandwich South

in account with

John Lynch, contractor

To 132 rods of ditching from stake 0
North side of Talbot Road to satke 11
~~at~~ near Blind line 132 rods at 87¢ per rd. 114.84

To Blind line to Delisle Drain on Talbot
Road 142½ rods at 96¢ per rod. 136.80

Amount Estimated cost of construction 251.64

Removing Brush small trees &c 20.00

Cutting and replacing fences to allow
teams to pass through 4.00 24.00

Total estimated cost of construction \$375.64

Add for casting earth excavated from ditch
on east side of drain instead of west side
for 66 rods north of South Talbot Road. *as per Agreement* 8.58

Total amount due contractor on
completion of his contract \$284.22

CR.

By retained for failure to properly spread
the earth excavated from drain on part
of Hugh Lennon's lands 5.25

By failure to remove two trees and stump
from line of drain 10.00

Amount of *contra* account 15.25 15.25

Balance due \$268.97

Payments made to contractor as follows.
1913

Nov. 15	Paid per council	75.00
Dec. 6	" " "	50.00
Dec. 15	" " "	35.00
1914		
May 23	" " "	50.00
Dec 14	" " "	<u>-58.97</u>

Amount paid in full for work completed to date. \$268.97

Owen McCay

OWEN MCKAY

ONTARIO AND DOMINION LAND SURVEYOR AND
CIVIL ENGINEER

MEMBER CANADIAN SOCIETY OF CIVIL ENGINEERS

WALKERVILLE, ONT., March 3rd, 1915.

Mr J.H. Rodd.

Solicitor &c.

Victoria Block, Windsor, Ont.

Dear Sir.-- re John Lynch, vs, Township of Sandwich South.

Enclosed you will please find a copy of plan and Profile of the Malden Road Relief Drain and Estimate of Cost of the work and beg to report the following particulars thereon.

The Drain was sold by Public Auction to John Lynch at the Estimated Cost of construction \$251.64 and in addition to cost of excavation, he was entitled to receive \$20.00 for removing Brush, Small trees &c from the line of ditch and three feet from the edge thereof as per Specifications, a copy of which is attached to Plan and estimate, and \$4.00 for cutting fence where the ditch crosses from the west side of fence to east side thereof making the total amount due John Lynch on completion of his contract was \$275.64, but Mr Donavon, Councillor agreed with Lynch to cast the earth from the drain along Dawson's fence, South west part of Lot 295 to prevent pigs from getting under the fence into the drain and on his neighbors land, for which Lynch agreed to do at an advance of 13¢ per rod for a distance of 66 rods which added to the cost of work, \$8.58 making a total cost of \$284.22 from which we deducted \$5.25 for earth excavated from the drain which Lynch failed to spread and also the sum of \$10.00 for trees and stump which he failed to remove from the side of ditch which left a balance of \$268.97 due him, which has been paid to the Contractor.
